



MIAMIBEACH

OFFICE OF THE CITY MANAGER
LTC # 192-2014

LETTER TO COMMISSION

TO: Mayor Philip Levine and Members of the City Commission
FROM: Jimmy L. Morales, City Manager
DATE: June 6, 2014
SUBJECT: Miami Beach Convention Center

Attached please find updated timeline for the Convention Center renovation project. This update will be posted on the City's website.

Thank you.


Attachment

JLM//MH
F:\cmgr\\$\ALL\Convention Center\LTC's\LTC_MBCC Timeline_6-6-14.doc

RECEIVED
2014 JUN -6 PM 1:08
CITY CLERK'S OFFICE

Miami Beach Convention Center Renovation Key Commission Dates

Updated 5-30-14

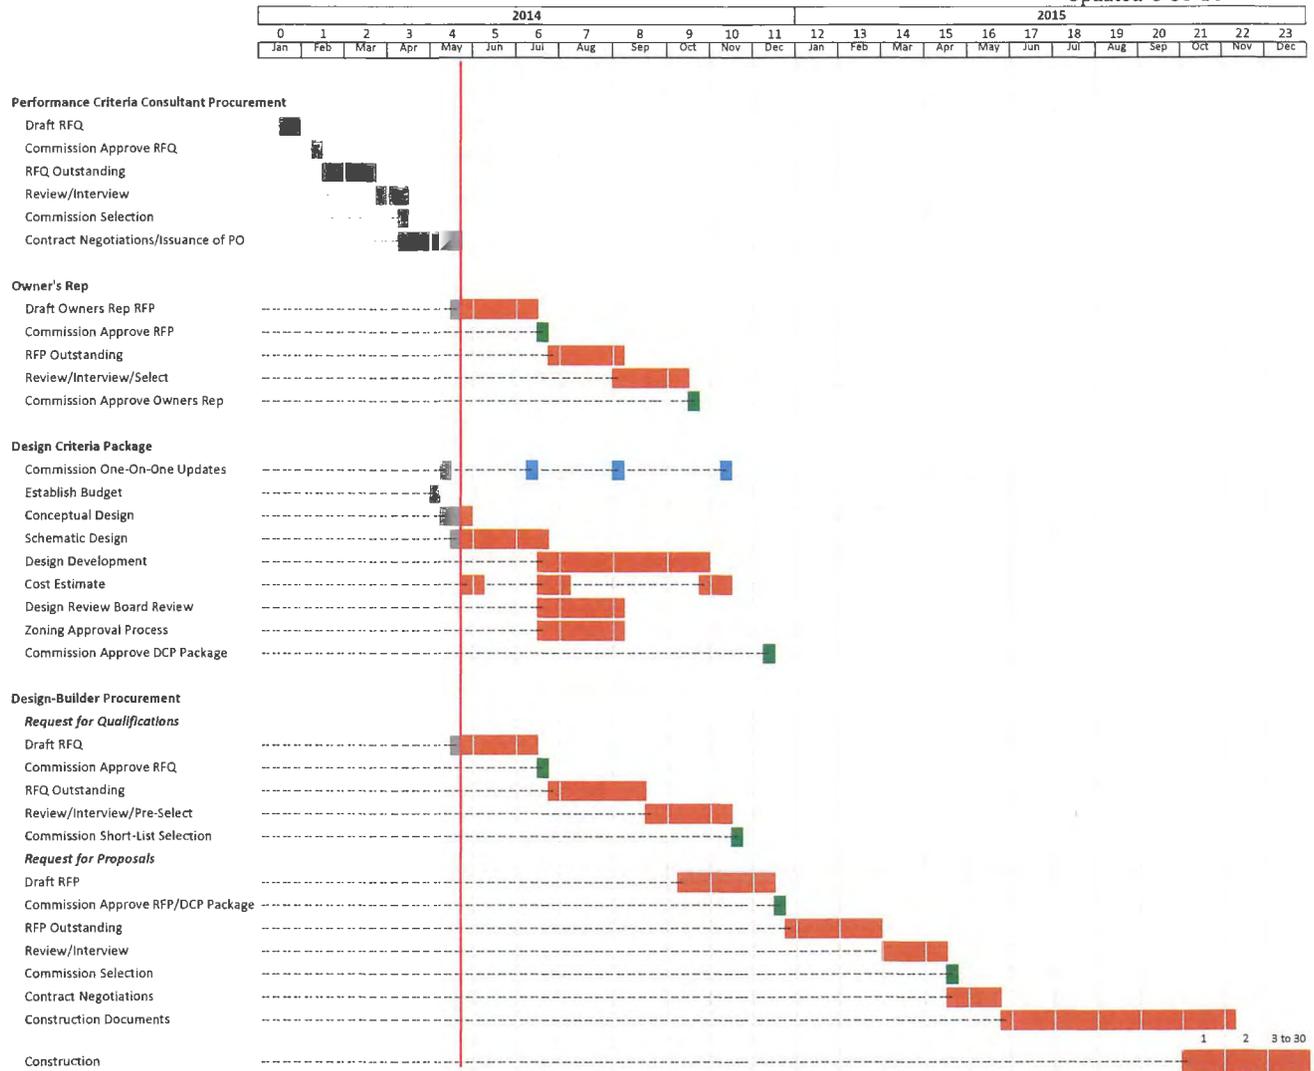

2014

- April 9 – Commission Refers construction booking policy to Finance Committee – Done.
- April 9 – Commission action on DCP selection – Done.
- April 30 – Finance Committee assesses construction booking policy – Done.
- May 13 - 14 – Commissioners participate in design visioning session – Done.
- May 28 – Commission approval of MBCC booking policy during construction – Done
- June 11 – Commission Presentation for Hotel Site Options
- July 7/8 – Commissioner one-on-one update of Conceptual Design and Budget
- July 23 – Commission Permission to issue RFP for Owners Oversight Rep. and RFQ for Design Build Firm
- August 5 – Presentation of schematic design to Design Review Board (DRB Discussion Item)
- September 2/3/4 – Commissioner one-on-one update of Schematic Design
- October 7 – Request approval of design from Design Review Board
- October 22 – Commission approval of Owners Oversight Representative
- November 11/12 – Commissioner one-on-one update on Schematic Design
- November 19 – Commission approval of Design Build short-list
- December 17 – Commission approval of the design criteria package and approval of Design Build RFP

2015

- April 15 – Commission selection of Design Builder
- July 1 – Turn on 1% tax
